
A+A_1959_10_26-38 13.05.2005 15:24 Uhr Seite 30

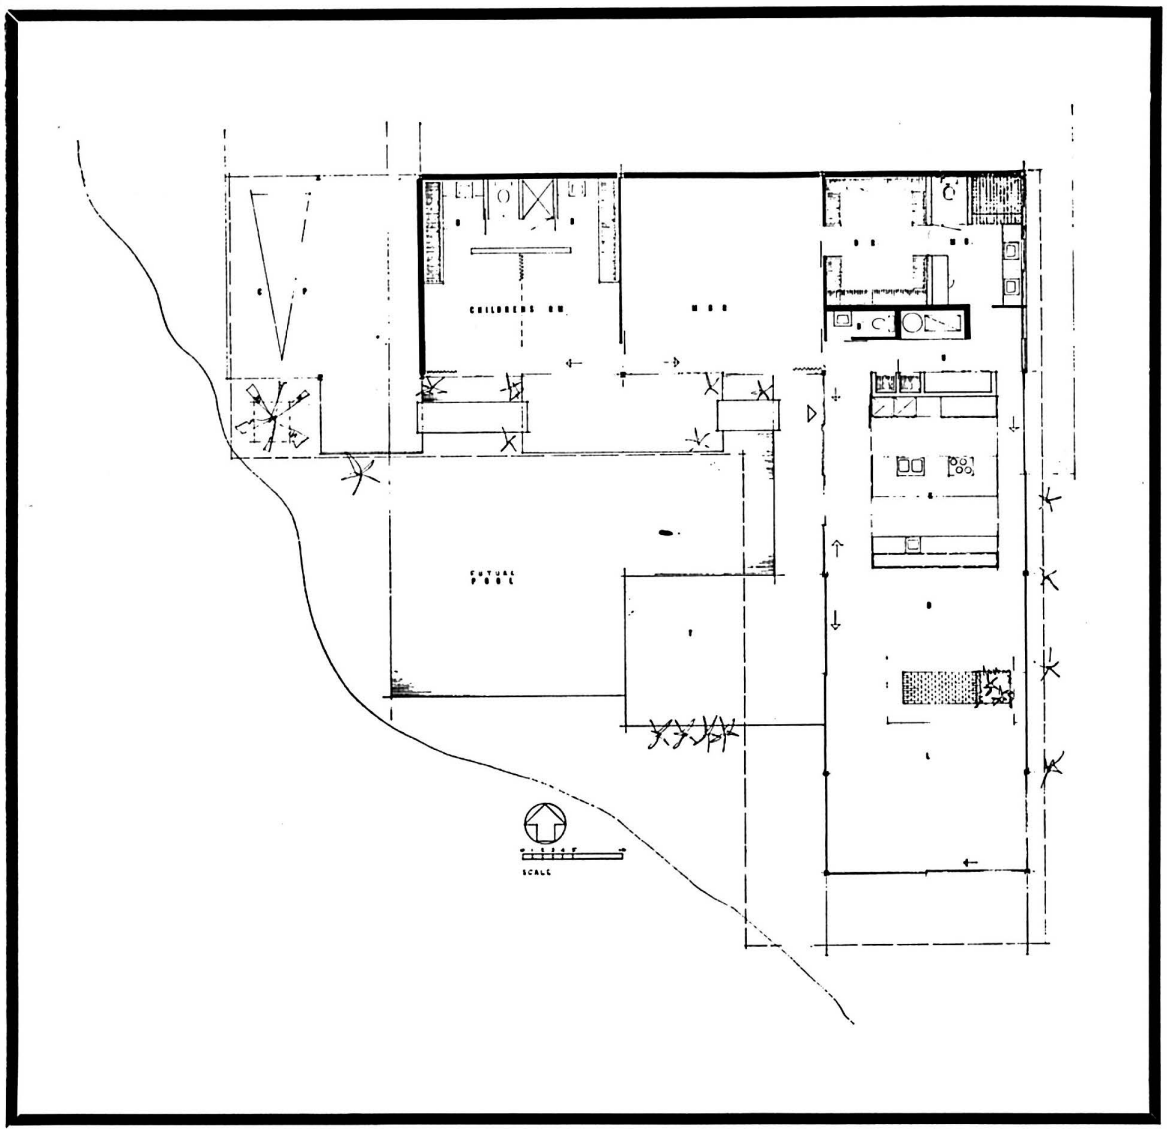


The construction photographs shown here were taken at the early stages of construction with the structural steel frame and the Bellevue steel sliding doors in place. The house at this stage is ready for steel roof deck and concrete grade beams. The foundation photographs show the reinforcing steel in what will be the system of cantilevered grade beams. The piers are not under the columns in this case but are set back from five to seven feet. In this way any possibility of damaging erosive action is eliminated. The columns are bearing at the ends of the concrete beams and are encased with twelve inches of concrete for resistance to seismic forces. With glass on all exterior walls except the street side, all horizontal forces can be resisted in this manner.


A working platform is constructed at one corner of the house and lot and is 125 feet above the first street directly below. Although the house is situated on a precipice the ground conditions are excellent with no extraneous water problems and without fill.


The sequence of construction calls for the setting of the base first, erection of steel frame and roof deck, installation of sliding door frames and wall decking, pouring of piers and grade beams, rough mechanical and electrical ducts and pipes, pouring of finish slab and finish, in that order. The usual sequence of fabrication on these houses was complicated by the fact that the piers are not directly under the columns. Special arrangements had to be made to support the columns before pouring structural concrete. The finish slab will be poured up to about the sill of the sliding door frames. The finish floor can thus be determined at this time by noting the location of the door sills.

(Continued on page 35)


PROGRESS REPORT — CASE STUDY HOUSE NO. 22 BY PIERRE KOENIG, ARCHITECT

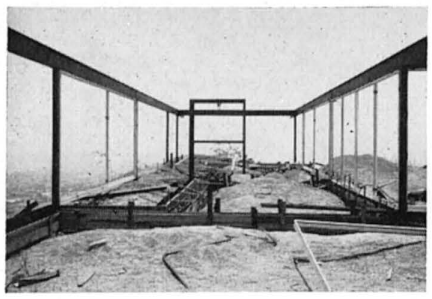



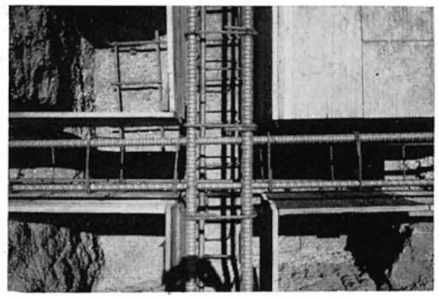



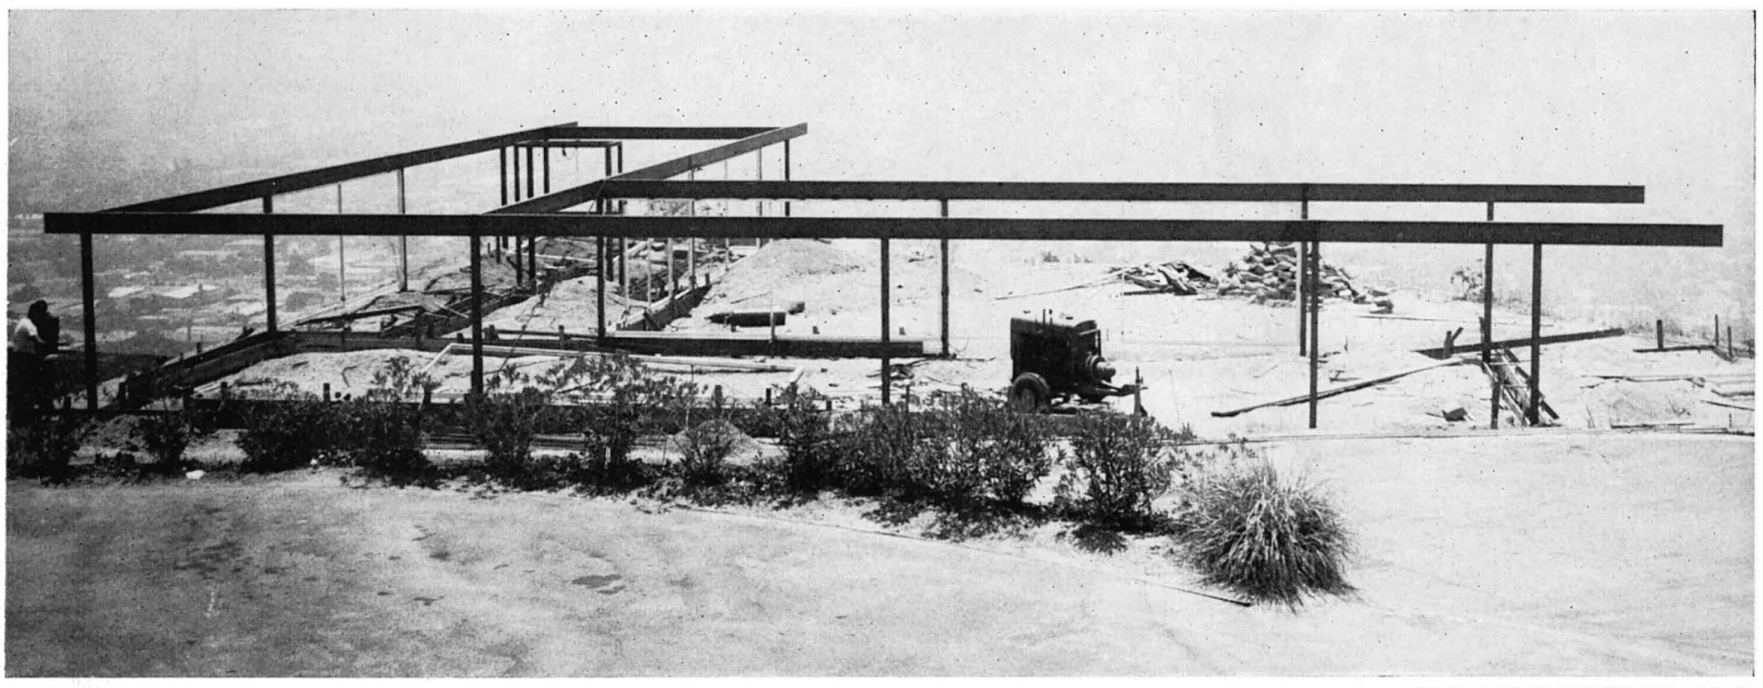

PHOTOGRAPHS BY KENNETH KNOLLENBERG
